

CHAPEL REPORT

A PUBLICATION
OF
MARTIN LUTHER
COLLEGE
NEW ULM, MN

Revised 11-20-09

M L C

Chapel of the Christ construction update


Exterior work: Metal trim panels are being installed. The cupola has been delivered (*pictured below*) and will be installed when the ground around the chapel freezes (so the crane will not damage the final landscape grade). Sidewalks, front patio, and parking lot are all completed.



Interior work: Walls are finished. Wood trim and lighting are nearing completion. Stone accents are being installed. Floor tile installation is complete. Carpet installation has begun. (*pictured, baptismal font with altar area in background*)



Organ construction is well underway at the Schantz Organ Co. in Orrville, Ohio. Finishing work for the organ area is nearing completion. Organ delivery is scheduled during the first week in December. Assembly is estimated at 4-6 weeks, with another 4-6 weeks to voice the pipes. (*picture from Schantz, schantzorgan.com; click on "in the shop"*)

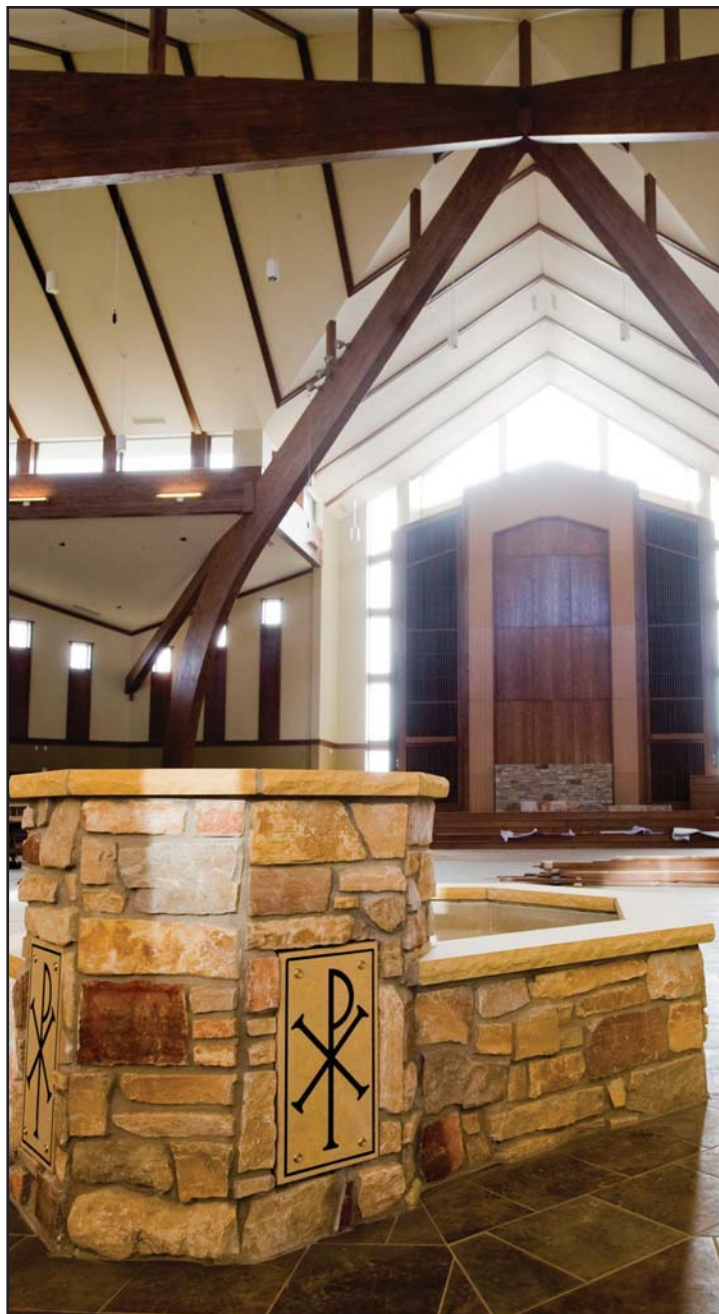

Dedication Weekend April 10 & 11, 2010

Saturday, April 10: Dedication Service 7:00 pm

Sunday, April 11: Dedication Service 2:30 pm

For more information visit www.mlc-wels.edu
